

Fiber to the Premise

Monthly Dashboard: February 2020

Monthly Highlights



Boring at Horseshoe Hut

- "2020 it's going to be a big year for Pulse!" Update posted online - view at www.LovelandPulse.com
- Established connectivity and tested communication between each hut

Fiber to the Premise Health Gauge





SCHEDULE

BUDGET

Notes:

Schedule: 23 weather days since November 2019 has impacted production rates, but remain within seasonal expectations

Budget: Costs to date higher than anticipated as final design quantities were finalized, but are expected to stay within current budget

MILESTONES COMPLETED SINCE LAST REPORT

- Number of areas with boring complete: 3
- Number of areas with fiber installation complete: 0

MILESTONES IN PROGRESS

- Additional areas moving forward
- Core network fiber installation in progress
- Hut equipment integration underway

MILESTONES NEXT STEPS

 Complete fiber installation in first area


LOST TIME SAFETY INCIDENTS TO DATE: 0









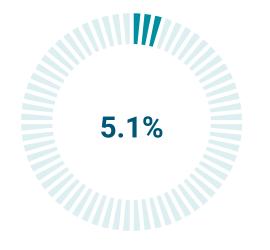

Network Construction Progress

Total Bore Length: **1,920,000**'

Completed Bore Length: **70,530**'



Total Construction Budget¹

Budget: **\$74,073,002**

Expenditure to Date: \$4,143,640

*Reported through: November 25, 2019 – February 29, 2020

¹Includes costs accrued for installation of active network equipment at huts



Horseshoe Substation - Hydro Boring

Substation Connections

Traffic Control







