



Installing railroad crossing casing pipe

## TAKE RATE INFORMATION



**RESIDENTIAL**



**BUSINESS**

### Project Milestones

- 0-32%: Planned Ramp-Up During Construction
- 32%: Business Plan Break Even After Full Buildout
- 42%: Expected Take Rate After Full Buildout
- 42-53%: Projections Exceeded

Take Rate is the percentage of potential residents or businesses that actually subscribe for Pulse service. To learn more about Pulse's Take Rate visit: [www.LovelandPulse.com/TakeRate](http://www.LovelandPulse.com/TakeRate)

## FIBER TO THE PREMISE HEALTH GAUGE



**SCHEDULE**



**BUDGET**

Notes:  
 Schedule: Thirty five weather days since November 2019 have impacted production rates but remain within seasonal expectations.  
 Budget: Costs to date higher than anticipated as final design quantities were finalized, but are expected to stay within current budget.

## MILESTONES COMPLETED SINCE LAST REPORT

- Installation and connection of Big Thompson Elementary School to the Pulse network.
- Number of completed areas with boring complete: 29
- Number of areas with fiber installation complete: 9


## MILESTONES IN PROGRESS

- A controlled release of Pulse residential services within several areas of Loveland continues to ensure that back-office processes and procedures are working as intended.

## MILESTONES NEXT STEPS

- Opening of new areas for customer sign-ups.
- Release of business services.


## LOST TIME SAFETY INCIDENTS TO DATE: 1

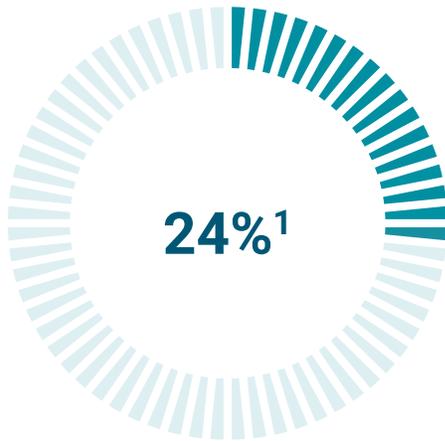

## Network Construction Progress

**Total Bore Length:**  
2,115,070'<sup>3</sup>

**Completed Bore Length:**  
520,061'

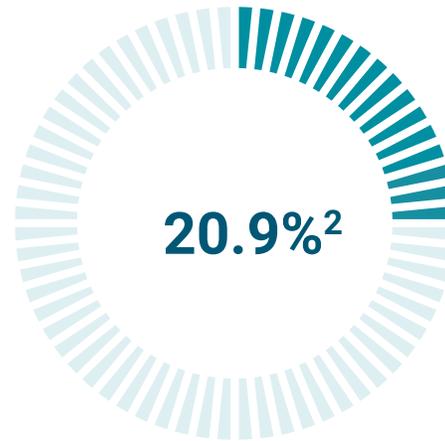

## Total Construction Budget

**Budget:**  
\$75,233,438<sup>4</sup>

**Expenditure to Date:**  
\$17,056,284

\*Reported from: November 25, 2019 – September 30, 2020

<sup>1</sup> Construction progress includes active network, and Hut installation in addition to Overall bored length

<sup>2</sup> Invoicing follows completed work

<sup>3</sup> Total boring updated based on final design estimate

<sup>4</sup> Budget total updated/corrected



Back Reamer



Got my Gig



Concrete Repair
