




Boring Site Walk

TAKE RATE



RESIDENTIAL

ACTIVE SERVICE AREA



Project Milestones

- 0-32%: Planned Ramp-Up During Construction
- 32%: Business Plan Break Even After Full Buildout
- 42%: Expected Take Rate After Full Buildout
- 42-53%: Projections Exceeded

Notes:
 Take Rate: Take rate is the percentage of total potential residential customers in active areas that subscribe for service.
 Learn more at www.LovelandPulse.com/TakeRate
 Active Service Area: Percentage of residents and businesses that are currently servicable by Pulse.

FIBER TO THE PREMISE HEALTH GAUGE



SCHEDULE

Notes:
 Schedule: One hundred and six weather days since November 2019 have impacted production rates but remain within seasonal expectations.
 Budget: Costs to date higher than anticipated as final design quantities were finalized, but are expected to stay within current budget.



BUDGET

TYPICAL SERVICE AREA SCHEDULE

- From the time that network construction begins in a neighborhood, we are typically able to begin providing service within six to nine months.

MILESTONES COMPLETED SINCE LAST REPORT

- Number of completed areas with boring complete: 114
- Number of areas with fiber installation complete: 103
- New Downtown areas available for commercial services

MILESTONES IN PROGRESS


- A controlled release of Pulse services.
- Construction in the Big Thompson Canyon for the CCSG program
- Pulse network construction in the Downtown area continues
- Weather conditions improve to permit burying of temporary winter service drops

MILESTONES NEXT STEPS

- Opening of new areas for customer sign-ups.
- Release of Pulse Rollout Map - Coming May 2022!

LOST TIME SAFETY


INCIDENTS TO DATE: 1

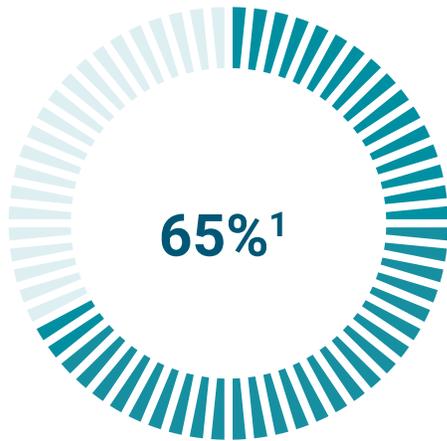

Network Construction Progress

Total Bore Length:
2,505,355'³

Completed Bore Length:
1,734,450'

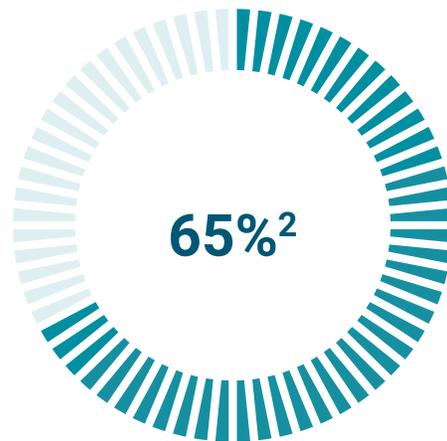

Total Construction Budget

Budget:
\$75,941,664⁴

Expenditure to Date:
\$53,407,526


*Reported from: November 25, 2019 – April 30, 2022

¹ Construction progress includes active network, and Hut installation in addition to overall bored length

² Invoicing follows completed work

³ Total boring updated based on final design estimate

⁴ Budget total updated/corrected

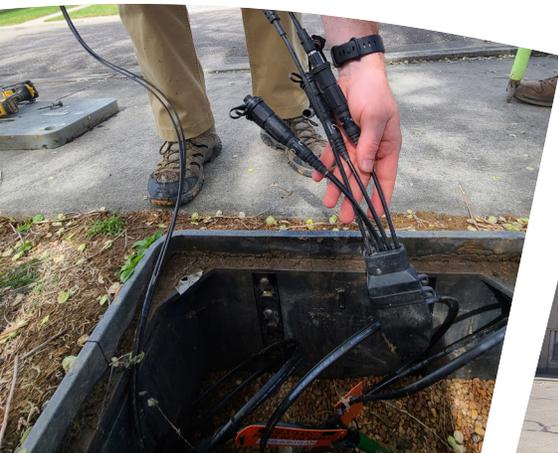

Vault Inspection



Downtown Potholing



As-Built Surveys
