

# Fiber to the Premise

Monthly Dashboard: May 2023




Boring

# **TAKE RATE**

# **ACTIVE SERVICE AREA**





# RESIDENTIAL

#### **Project Milestones**

0-32%: Planned Ramp-Up During Construction 42%: Expected Take Rate After Full Buildout

32%: Business Plan Break Even After Full Buildout 42-53%: Projections Exceeded

Notes: Take Rate: Take rate is the percentage of total potential residential customers in active areas that subscribe for service Learn more at <a href="https://www.LovelandPulse.com/TakeRate">www.LovelandPulse.com/TakeRate</a>
Active Service Area: Percentage of residents and businesses that are currently serviceable by Pulse.

# FIBER TO THE PREMISE HEALTH GAUGE





# **SCHEDULE**

#### **BUDGET**

Schedule: One hundred and forty-three weather days since November 2019 have impacted production Softwards. One indirect and office when the ways since woverhoer 2019 have impacted production rates but remain within seasonal expectations.

Budget: Costs to date higher than anticipated as final design quantities were finalized, but are expected to stay within current budget.

# **TYPICAL SERVICE AREA SCHEDULE**

 When network construction begins in a neighborhood, we typically begin providing service within six to nine months.

# **MILESTONES COMPLETED** SINCE LAST REPORT

- Number of completed areas with boring complete: 169
- Number of areas with fiber installation complete: 162

# **PULSE NETWORK CONSTRUCTION MAP**

Present-day snapshot of Pulse network construction and service availability www.LovelandPulse.com/Map

# **MILESTONES IN PROGRESS**

 Inter-governmental agreement with Larimer County for 3 additional under-served areas

#### **MILESTONES NEXT STEPS**

- Completion of Loveland Pulse construction within city limits (Phase 1)
- Launch WorkPass


**LOST TIME SAFETY INCIDENTS TO DATE: 1** 










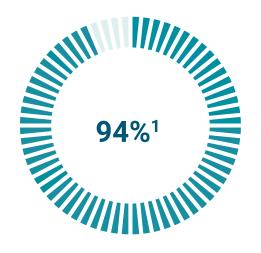

Network
Construction Progress

**Total Bore Length:** 2,279,179'<sup>3</sup>

Completed Bore Length: 2,260,126'

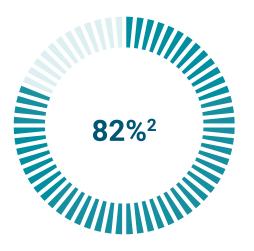

Total
Construction Budget

**Budget:** \$90,941,664<sup>4</sup>

Expenditure to Date: \$74,345,400

\*Reported from: November 25, 2019 - May 31, 2023

<sup>1</sup>Construction progress includes active network, and Hut installation in addition to overall bored length

<sup>2</sup> Invoicing follows completed work

<sup>3</sup>Total boring updated based on expected final quantities

<sup>4</sup> Budget total updated/corrected







Infrastructure Surveying

**Hydro Excavation** 

Fiber and Buffer Tubes







