




Conduit Boring

### TAKE RATE INFORMATION



26%

#### RESIDENTIAL

##### Project Milestones

- 0-32%: Planned Ramp-Up During Construction
- 32%: Business Plan Break Even After Full Buildout
- 42%: Expected Take Rate After Full Buildout
- 42-53%: Projections Exceeded

Take Rate is the percentage of potential residents or businesses that actually subscribe for Pulse service. To learn more about Pulse's Take Rate visit: [www.LovelandPulse.com/TakeRate](http://www.LovelandPulse.com/TakeRate)

### FIBER TO THE PREMISE HEALTH GAUGE



#### SCHEDULE



#### BUDGET

Notes:  
 Schedule: Ninety five weather days since November 2019 have impacted production rates but remain within seasonal expectations.  
 Budget: Costs to date higher than anticipated as final design quantities were finalized, but are expected to stay within current budget.

#### TYPICAL SERVICE AREA SCHEDULE

- From the time that network construction begins in a neighborhood, we are typically able to begin providing service within six to nine months.

#### MILESTONES COMPLETED SINCE LAST REPORT

- Number of completed areas with boring complete: 109
- Number of areas with fiber installation complete: 91
- Release of PulseTV Everywhere


#### MILESTONES IN PROGRESS

- A controlled release of Pulse services.
- Construction in the Big Thompson Canyon for the CCSG program
- Pulse network construction in the Downtown area.
- Transition from Emergency Broadband Benefit Program to Affordable Connectivity Program - [www.LovelandPulse.com/ACP](http://www.LovelandPulse.com/ACP)

#### MILESTONES NEXT STEPS

- Opening of new areas for customer sign-ups.


#### LOST TIME SAFETY INCIDENTS TO DATE: 1

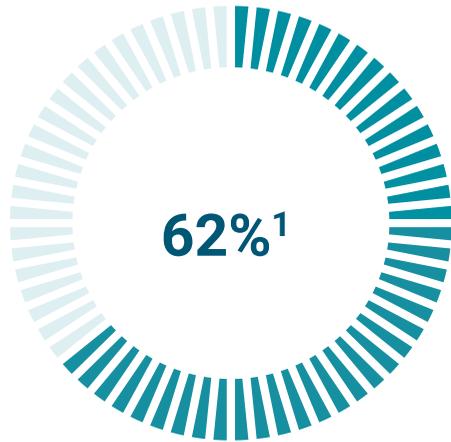

**Network  
Construction Progress**

**Total Bore Length:**  
2,505,355'<sup>3</sup>

**Completed Bore Length:**  
1,553,689'

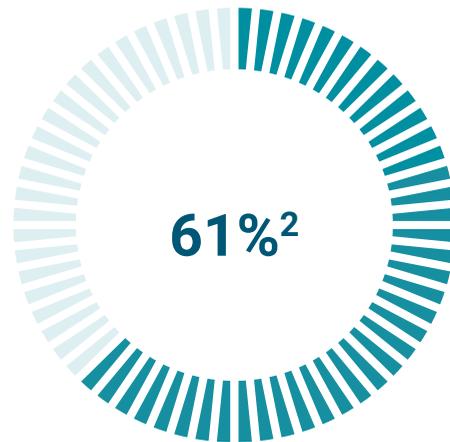

**Total  
Construction Budget**

**Budget:**  
\$75,941,664<sup>4</sup>

**Expenditure to Date:**  
\$46,724,843

\*Reported from: November 25, 2019 – January 31, 2022

<sup>1</sup> Construction progress includes active network, and Hut installation in addition to overall bored length

<sup>2</sup> Invoicing follows completed work

<sup>3</sup> Total boring updated based on final design estimate

<sup>4</sup> Budget total updated/corrected



Utility Potholing



Locating



Vault Inspection
