




Boring and Conduit Installation

### TAKE RATE



### RESIDENTIAL

### ACTIVE SERVICE AREA



#### Project Milestones

- 0-32%: Planned Ramp-Up During Construction
- 32%: Business Plan Break Even After Full Buildout
- 42%: Expected Take Rate After Full Buildout
- 42-53%: Projections Exceeded

Notes:  
Take Rate: Take rate is the percentage of total potential residential customers in active areas that subscribe for service.  
Learn more at [www.LovelandPulse.com/TakeRate](http://www.LovelandPulse.com/TakeRate)  
Active Service Area: Percentage of residents and businesses that are currently serviceable by Pulse.

### FIBER TO THE PREMISE HEALTH GAUGE



### SCHEDULE



### BUDGET

Notes:  
Schedule: One hundred and forty-one weather days since November 2019 have impacted production rates but remain within seasonal expectations.  
Budget: Costs to date higher than anticipated as final design quantities were finalized, but are expected to stay within current budget.

### TYPICAL SERVICE AREA SCHEDULE

- When network construction begins in a neighborhood, we typically begin providing service within six to nine months.

### MILESTONES COMPLETED SINCE LAST REPORT

- Number of completed areas with boring complete: 167
- Number of areas with fiber installation complete: 160
- Adaptive WiFi+ launched
- Residential internet packages updated
- Final 10 Gig component connected

### PULSE NETWORK CONSTRUCTION MAP

- Present-day snapshot of Pulse network construction and service availability  
[www.LovelandPulse.com/Map](http://www.LovelandPulse.com/Map)

### MILESTONES IN PROGRESS

- Inter-governmental agreement with Larimer County for 3 additional under-served areas

### MILESTONES NEXT STEPS

- Completion of Loveland Pulse construction within city limits (Phase 1)
- Launch WorkPass


**LOST TIME SAFETY INCIDENTS TO DATE: 1**



## Network Construction Progress

**Total Bore Length:**  
2,279,179'<sup>3</sup>

**Completed Bore Length:**  
2,240,408'

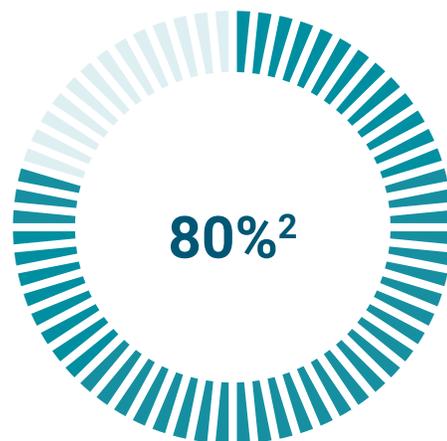

## Total Construction Budget

**Budget:**  
\$90,941,664<sup>4</sup>

**Expenditure to Date:**  
\$72,957,474

\*Reported from: November 25, 2019 – April 30, 2023

<sup>1</sup> Construction progress includes active network, and Hut installation in addition to overall bored length

<sup>2</sup> Invoicing follows completed work

<sup>3</sup> Total boring updated based on expected final quantities

<sup>4</sup> Budget total updated/corrected



Boring Path Quantity Measurements



Fiber and Equipment



Conduit Prep for Vault Installation
